BERABAN

LUXURY LOFT

CONSTRUCTION UPDATE

July 2025



Forbes

BERABAN

PERTAMA



OVERALL PROGRESS We are progressing steadily through the structural phases. The basement structural works for Towers 1 to 6 commenced on 1 August 2024. The targeted completion for this second phase, extending through to the top floor, is set for October 2025.

Basement

Phase 1:

100% complete – All structural elements, including footplates, pedestal columns, basement slabs, ground floor columns, retaining walls, and pit lifts, have been finalised.

Phase 2:

- 1. Footplate and pedestal columns: 100% complete
- 2. Overall basement structure: 53% complete
 - Slab: 50%
 - Ground floor columns: 55%
 - Retaining wall: 24%
 - Pit lift: 84%



Ground Floor to Roof

Ground floor (Phases 1 & 2 combined): 66% complete

- Ground floor slab: 68%
- Columns to 1st floor: 65%
- Pit lift: 66%

1st Floor:

Overall Progress: 33%. Work is actively progressing on slabs, columns, and pit lift structures.

2nd Floor:

Initial works commenced, overall progressing 16% with only slab construction is currently at 48% completion.














Quality and Safety Measures

We are committed to delivering a high-quality, structurally sound development. Current control measures include:

- Ongoing joint dimension surveys to ensure precision alignment
- Continuous monitoring of lavatory pipe installations in the basement
- Regular inspections and reviews of rebar work for footplates, slabs, and columns, supported by detailed checklists





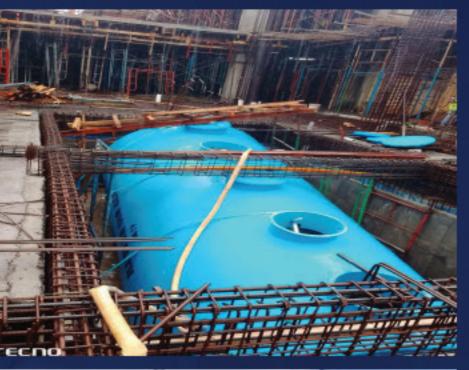









POWERED BY



PERTAMA BERABAN

LUXURY LOFT

PROPERTY
